SHFC HIGH DENSITY HOUSING PROGRAM

As of January 31, 2017

SHFC BOARD APPROVED PROJECTS (As of January 2017)

		TAI	RGETS (ISFs)		
2013	2014	2015	2016	2017	TOTAL
2,300	6,400	7,754	3,696	*	20,150

	ACTUAL PERFORMANCE (ISFs) – BOARD APPROVED										
20	13	20)14	20	15	2	016	2	017	TOT	TAL .
In City	Near City	In City	Near City	In City	Near City	In City	Near City	In City	Near City	In City	Near City
212	-	5,043	4,114	1,937	5,955	2106	546	-	-	9,298	10,615
										46.69%	53.31%

- Total approved projects from 2013-2016 = <u>19,913 ISFs</u>
- This is 98.82% of the 2013-2016 target of 20,150 as submitted to `DBM
- 46.69% In City; 53.31% Near City
- * Phase 2 of Peoples Plan Ville HOAI with 200 ISF

TIDITI NOJECI SIATOS (AS OLJANICAL)	ECT STATUS (As of January	(2017)
-------------------------------------	---------------------------	--------

DA D'TICILI A D C	Duningto	ISFs (units)		
PARTICULARS	Projects	In City	Near City	Total
A. Phase 1 (Land Acquisition)	38	9,298	10,615	19,913
Land Acquired For Payment	31 7	8,056 1,242	10,069 546	18,125 1,788
B. Phase 2 (Site Dev't & Bldg Cons)	38	9,298	10,615	19,913
- Occupied - On-going Construction:	12 15	730		730
Completed Units of On-going Remaining Units for Completion		2,480 2368	2,205 6,260	4,685 8,628
For release of 15% Mobilization FundAwaiting Permits (for Phase 2 Board Approval)	3 8	1,160 2,560	720 1,430	1160 3,990

Land Acquired – Amvaca (1,440), Goldmine (104) Ernestville (212), Corrinai (109), Pascualer (994), MWAHC (864), Blue Meadows (496), St. Hannibal (65), Bistekville Mabuhay (42), Bistekville 1 Blk 5 (36), Bistekville 2 Blk 2 (78), Bistekville 2 Blk D (24), Bistekville 2 Blk 16 (63), Bistekville 2 Blk 6 (69), Bistekville 1 Blk 12 (14), Hopeville (399), Genesisville (720), AMC (390), Bistekville 2 Blk 3 (63); Umalpas (884), Alpas 1 (546), South Morning View (1,180), RSP (1,504), BV8 de Muzon (1,589), SMP (800), Ciudad de Strike (1,440), Upcaville (720), Gumamela (1,406), BSML (1,324), Gloriaville (378), Jesse M Robredo Village (172)

For Payment – Villa Makabayan (192), GPHOAI (440), Bistekville 2 Blk. 41/42 (78), Alpas 2 (546), Marangal (282), People's Plan Ville (200), Bistekville 1 Blk 14 Occupied – All Bistekville Projects (517), Goldmine (104) and Corrinai (109)

On going Construction- Amvaca (1,440), Ernestville (212), Pascualer (994); Alpas (546), South Morning View (1,180), RSP (1504), BV8 de Muzon (1589), MWACH (864), Ciudad de Strike (1,440), SMPHOAI (800), Blue Meadows HOAI (496), St. Hannibal HOAI (65), Hopeville (399), Gumamela (1,406), Gloriaville (378)

For release of 15% Mobilization—GPHOAI* (440), Upcaville (720), Genesis Ville (720)

Awaiting Permits – AMC (390), Villa Makabayan (192), BSML* (1324), Umalpas (884), Alpas 2 (546), Marangal (282) Jesse M Robredo Village (172)*, People's Plan Ville (200)*

Target completion of on going projects, recently approved projects and projects awaiting permits

	No. of projects/ISFs	2016	2017	2018
Phase 2 (on going Projects)	15 ; 13,313	4,685	8,250	378
Recently Approved Projects (for release of 15% mobilization fund)	2 ; 1,160		1,050	110
Awaiting Permits (for Ph2 Board approval)	9 ; 4,710		4,210	500

	2016	2017	2018
Completed	4,685	13,888	769
Occupied	730 (12 projects)	15,665 (16 projects)	2,947 (3 projects)

TENURIAL SECURITY

	No. of Projects	No. of ISFs
Ownership	15	2,447
Usufruct	23	17,466
	38	19,913

Ownership – Amvaca, Goldmine, Ernestville, Corrinai,, St. Hannibal, Bistekville Mabuhay, Bistekville 1 Blk 5, Bistekville 2 Blk 2, Bistekville 2 Blk D, Bistekville 2 Blk 16, Bistekville 2 Blk 6, Bistekville 1 Blk 12, Bistekville 2 Blk 3, Bistekville 2 Blk. 41/42, Bistekville 1 Blk 14

Usufruct – Pascualer, MWAHC, Blue Meadows, Hopeville, Genesisville, AMC, Umalpas, Alpas 1, South Morning View, RSP, BV8 de Muzon, SMP, Ciudad de Strike, Upcaville, Gumamela, Gloriaville, Villa Makabayan, GPHOAI, BSML, Alpas 2, Marangal, Jesse Robredo Village, People's Plan Ville

FUND UTILIZATION HIGHLIGHTS as of January 31, 2017

PARTICULARS	TOTAL (in PhP M)
I. GAA	9,763.76
II. SARO RECEIVED	8,657.39
III. NCA RECEIVED	3,772.98
IV. OBLIGATIONS	7,849.99
V. DISBURSEMENTS	3,630.15
VI. UNISSUED SARO (I - II)	827.35
VII. UNRELEASED NCA* (II - III)	4,884.41
VIII. CASH BALANCE (III – V)	142.83

SARO – 88.66% of GAA

NCA (Cash) Received

- 38.64% of GAA
- 43.58% of SARO

Obligations

(Board Approved Projects)

- 80.39% of GAA
- 90.67% of SARO

Disbursements

- 37,18% of GAA
- 41.93% of SARO
- 96.21% of Cash Released

^{*}NCA depends on construction progress. Exclusive of 350M issued by DILG for Jessie M. Robredo Village Phase 2

CHALLENGES & RECOMMENDATION

Issues & Concerns	Recommendation
A. ON LAND ACQUISITION	
■ Delay in the issuance of the BIR CGTE & CAR	 Establish an express lane (1 month) for programs that have been mandated by law to be exempt from CGT & priority projects & programs identified by NEDA
 HDH using usufruct tenurial arrangement is not exempt from CGT 	 Exempt HDH, a NEDA certified priority program for the ISF from CGT
 Objection of LGUs to absorb ISFs residing outside their cities 	 Provide incentives to receiving LGUs (transfer of IRA from sending to receiving to ensure funds for social services)
B. ON SITE DEVELOPMENT & HOUSE CONST	RUCTION
■ Difficulty to secure permits from the LGUs	 Establish institutional arrangement with DILG and concerned LGUs

CHALLENGES & RECOMMENDATION

Issues & Concerns	Recommendation
C. TITLING FOR HDH	 Harmonize the Condominium Law with the ISF Housing under the HDHP
D. LACK OF BUDGET	 Institutionalize HDHP by including it in the CISFA (Comprehensive & Integrated Shelter Finance Act)

Name of Project	Ernestville HOAI
No. of MBs	212
Relocation Site	Brgy. Gulod, Novaliches, Quezon City
Date of Approval Phase 1: Phase 2:	Feb 28, 2013 Feb 28, 2013 & May 27, 2015
Project Cost/ Loan Per ISF	PhP 67,692,566.04/ PhP 319,304.56
Date Started	10/12/2015
Target Date of Completion	10/13/2016
No of Buildings	12
No. of MBs per Building	varies
Type of Building	Two Storey with provision for loft
Floor Area	25.60 square meter
Amortization Fee	Php 773.84
Status	100% (AO JAN 2017)

Name of Project	Goldmine Interior HOAI
No. of MBs	104
Relocation Site	Brgy. Nagkaisang Nayon, Novaliches, Quezon City
Date of Approval	
Phase 1:	October 21, 2013
Phase 2:	October 21, 2013
Project Cost/	PhP 41,600,000.00/
Loan Per ISF	Php 400,000.00
Date Started	4/11/2015
No of Buildings	6
No. of MBs per Building	Varies
Amortization Fee	Php 1,692.97
Floor Area	28.0 square meters

Two Storey with provision for loft Type of Building 100% Completed; Members paying monthly amortization since May 17,

2016 with 151.27% CER as of

December 2016



Status







Block 3





Block 2





Block 6



Block 4





Block 5

Block 1

Name of Project	AMVACA	
No. of MBs:	1440	
Relocation Site:	Sitio La Mesa St., Brgy. Ugong, Valenzuela City	
Date of Approval		THE RULE WILLIAM STATES OF THE REAL PROPERTY OF THE
Phase 1:	Dec 27, 2013	GET TO ZOTE
Phase 2:	Sept 1, 2014	
Project Cost/	Php 576,000,000.00/	
Loan Per ISF	Php 450,000.00	
Date Started:	10/11/2014	
Target Date of Completion	September 2, 2016	06/10/2016
No of Buildings:	30	
No. of MBs per Building	48	
Type of Building	Three Storey with loft	
Floor Area	39.73 sq. meters	
Amortization Fee	Php 954.32	
Status (AO August 2016)	95.32% overall work accomplishment 95.71% for site development and building 92.78% for the loft	

Name of Project	Corrinai Housing Cooperative	
No. of MBs:	109	
Relocation Site:	L. Francisco St., Zamora, Pasay City	
Date of Approval		
Phase 1:	May 26, 2014	
Phase 2	Feb 24, 2015	
Project Cost/	Php 54,173,000.00/	
Loan Per ISF	Php 4 ki50,000.00	
Date Started:	28-Mar-15	
No of Buildings:	1	
No. of MBs per	109	
Building		
Type of Building	Four Storey Unit with provision	
	for loft	
Floor Area	18 square meters	
Amortization Fee	Php 1,055.32	
Status	100% completed	

Name of Project	ALPAS PH1 HOAI	
No. of MBs:	546	
Relocation Site:	Brgy. Muzon, San Jose del Monte City, Bulacan	
Date of Approval		
Phase 1:	June 25, 2014	
Phase 2:	Nov 26, 2014	
Project Cost/	Php 245,699.999.32/	
Loan Per ISF	Php 391,617.95	
Date Started:	3/15/2015	
Target Date of Completion (Extension)	April 2017	
No of Buildings:	26	
No. of MBs per Building	21	
Type of Building	Three Storey unit with loft	
Floor Area	35 square meters	
Amortization Fee	Php 656.72 and Php 1,166.53	
Status	84.17% (AO 19 Nov 2016)	
		PICTURE TAKEN LAST FEB. 17, 2017

Name of Project	South Morning View HOAI	
No. of MBs:	1,180	
Relocation Site:	Brgy. Timalan, NAIC, Cavite	
Date of Approval		
Phase 1:	July 31, 2014	
Phase 2:	Aug 28, 2014	
Project Cost/	PhP472,000,000.00/	
Loan Per ISF	PhP274,007.29/ISF) under	
	USUFRUCT	







5/19/2015

Rowhouse with Loft

30.60 square meters

Php 656.72 and Php 1,166.53

Date Started:

Floor Area

Type of Building

Amortization Fee

Name of Project	RSP Village HOAI	
No. of MBs:	1,504	
Relocation Site:	Brgy. Gaya-gaya, San Jose del Monte City, Bulacan	
Date of Approval		
Phase 1:	Dec 12, 2014	
Phase 2:	April 24, 2015	
	Php661,760,000.00/	
Project Cost/	PhP355,470,15/ISF)	
Loan Per ISF	under Usufruct)	
Date Started:	8/27/2015	
Target Date of		
Completion:	8/28/2016	
No of Buildings:	47	
No. of MBs per Building/ Floor Area	32/ 24 square meters	
Type of Building	Two Storey with provision for loft	
Amortization Fee	Php 1,042.71	
Status	25.31% as of 17	
	Dogombor 2016	

Name of Project	Pascualer Ville ISF HOAI	
No. of MBs:	994	
Relocation Site:	Rolling Meadows, Novaliches, Quezon City	
Date of Approval		
Phase 1:	July 31, 2014	
Phase 2:	Aug 20, 2015	
Project Cost/	Php447,300,000.00/	
Loan Per ISF	(Php359,865.99/ISF (unde USUFRUCT)	
Date Started:	10/16/2015	
Target Date of Completion:	10/17/2016	
No of Buildings:	17	
No. of MBs per	Varies/33.80 square meters	
Building/ Floor Area	1	
Type of Building	Two Storey with Loft	
Amortization Fee	Php 1,055.60	
Status	82.67% (AO Nov 2016)	
	PICTURE TAKEN LAS	ST FEB. 21, 2017





No. of MBs: 1,589

Relocation Site: Sitio Partida, San Jose del Monte Bulacan

Date of Approval Phase 1: June 29, 2015

Phase 2: January 27, 2016

Project Cost/ Php627,655,000.00

Loan Per ISF /PhP319,982.06/ISF) - under USUFRUCT

Date Started: 06/17/2016

06/17/2017 Target Date of Completion:

Floor Area 28.76 square meters

Type of Building Rowhouse with Loft

Php 938.61 Amortization Fee

Status 32.277% (AO January 2017)







Bulacan Date of Approval Phase 1: July 28, 2015 Phase 2: February 24, 2016 Php 337,222,033.57 Project Cost/ Loan Per ISF /PhP324,831.25/ISF) - under **USUFRUCT** Date Started: 07/22/2016 07/22/2017 Target Date of Completion: Floor Area 27.50 square meters Rowhouse with Loft Type of Building Status 15% mobilization fund released last July 12, 2016 PICTURE TAKEN LAST FEB. 17, 2017

Sandigan ng Maralitang

Sitio Partida, San Jose del Monte

Pilipino HOAI

800

Name of Project

Relocation Site:

No. of MBs:


			PICTURE TAKEN LAST FEB. 24, 2017		
	Name of Project	Ciudad de Strike HOAI-2			
	No. of MBs:	1440			
	Relocation Site:	Molino Road, Molino 1, Bacoor, Cavite			
	Date of Approval Phase 1: Phase 2: Project Cost/	August 20, 2015 February 24, 2016 Php 544,189,235.12			
	Loan Per ISF	/PhP363,804.82/ISF) - under USUFRUCT			
	Date Started:	07/25/2016			
	Target Date of Completion:	07/25/2017			
	Floor Area	30.0 square meters			
	Type of Building	Three Storey Building with Loft			
	Status	15.31% (AO Dec 28,2016)			



Name of Project	Kapitbahayan ng Blue Meadows	Loan Per ISF	/PhP375,000/ISF) - under USUFRUCT
No. of MBs:	HOAI 496	Date Started:	8/8/2016
Relocation Site:	Balintawak Subdivion, Brgy 175 Camarin, Caloocan City	Target Date of Completion:	8/9/2017
Date of Approval		Floor Area	21.50square meters
Phase 1: Phase 2:	January 26, 2015 May 11, 2016	Type of Building	Three/Two Storey Building with Loft
		Status	25.39% (AO Dec 2016)

Name of Project	St. Hannibal HOAI
No. of MBs:	65
Relocation Site:	E. Cornejo St. Pasay City
Date of Approval Phase 1: Phase 2:	June 25, 2014 March 21, 2016
Project Cost/ Loan Per ISF	Php 32,057,731.00 /PhP450,000/ISF
Date Started:	8/4/2016 8/4/2017
Target Date of Completion:	0/ 1/ 201 /
Floor Area	21.0square meters
Type of Building	Five Storey Building with Loft
Status	15% mobilization fund released last July 25, 2016







Name of Project	Hopeville Phase 2 HOA1	Date Started:	9/24/2016
No. of MBs:	399		9/24/2017
Relocation Site:	Brgy 171 District 1, Bagumbong Caloocan City	Target Date of Completion:	
Date of Approval	Caroocair City	Floor Area	22.0 square meters
Phase 1:	January 26,2015	Type of Duilding	Three Storey Building
Phase 2:	May 11, 2016	Type of Building	
Project Cost/ Loan Per ISF	Php 170,788,255.89 /PhP375,000/ISF	Status	15% mobilization fund released last September 14, 2016

g
gad,
l last





Gumamela Neighborhood Name of Project **Housing Cooperative** No. of MBs:

1,406

Brgy. Kaypian, San Jose del Monte

City, Bulacan

Date of Approval Phase 1: September 24,2015

Relocation Site:

Type of Building

Status

Phase 2:

May 11, 2016

Php 551,020,142.20

Project Cost/ /PhP300,000/ISF Loan Per ISF

Date Started: 9/25/2016

9/25/2017 Target Date of

Completion:

Floor Area 30.60 square meters

> Duplex 15% mobilization fund released last September 15, 2016




PICTURE TAKEN LAST FEB. 17, 2017

Bistekville 1 Subdivision

(Bistekville 1 Subdivision, Brgy. Payatas, Quezon City)



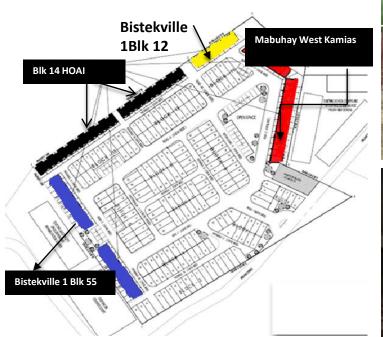





Bistekville 2 Subdivision

(Brgy. Kaligayahan, Novaliches, Quezon City)





HALLWAY

BLOCK 41



FRONT VIEW ALONG ALLEY 20



FRONT VIEW ALONG ALLEY 19







ELECTRIC & WATER METER



STAIRS



HALLWAY







SERVICE AREA

STAIRS

SPECIAL PROJECTS FOOTNOTES

Funded under the Special Funds* [DPWH Savings amounting to P1.087 Billion]

Project Name	Board Approval	No. of ISFs	Project Cost
Jesse Robredo HOAI (DOF Property)	11 May 2016	172	Php 60,653,120.00
Peoples Plan Village HOAI	11 May 2016	200	Php 291,687,340.00

^{*}Also includes 2 regular HDH Projects namely: GPHOAI (440 ISFs) and BSML (1,324 ISFs)

Jesse Robredo HOAI (DOF Property)

Origin:

Along Manila City waterways: Estero de Quiapo, Estero de San Miguel Legarda, Estero de San Miguel P. Casal and Estero de San Sebastian

Relocation Site:

DOF Natcoco Property
J. Nepomuceno St., (Calle Tanduay)
San Miguel, Manila

No. of ISFs:

172 families along Estero de Quiapo, Estero de San Miguel Legarda, Estero de San Miguel P. Casal and Estero de San Sebastian



Peoples Plan Village HOAI

Origin:

Along Pasig River and Estero de Magdalena

Relocation Site:

GSIS Property; Pureza Street Brgy. 628, Sta. Mesa Manila

No. of ISFs:

200 families living along Pasig River and Estero de Magdalena

